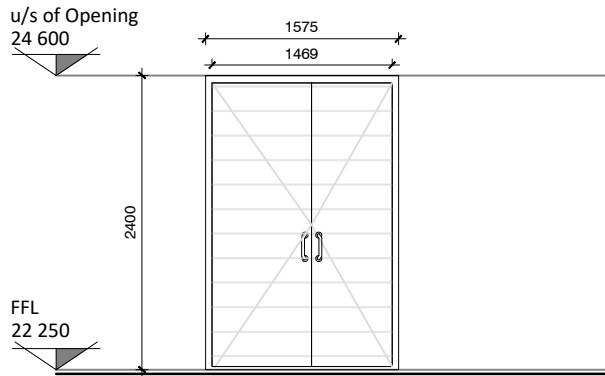


Interior/Exterior Solid Core Timber Door


- After the door has been fit contractor has to take all necessary measures to protect the unit from on site damage.

TYPICAL ELEVATION

QUANTITY 1

LOCATION Meet-me-Room

FRAME TYPE:

- 1575mmx2400mm Meranti timber door frame 70x108mm rebate. Contractor to order correct quantity left and right swing opening.

DOOR TYPE:

- 40mm thick solid core timber hardwood door. Faced both sides with commercial veneer.
- 1 x 813mm wide x 2350mm High 1x 656mm wide 2 2350mm high.

FINISH TO DOOR AND FRAME:

- Plascon Velvagio Satin to exterior new wood.
- Surface to be dry sound and clean. Wash knots and resinous areas with lacquer thinners (ILS1) and coat with woodcare knot seal (PK2) and apply one coat of plascon woodcare pretreatment (WWP1) overcoated within 48 hours with a moisture content, measured with a doser hygrometer (Or equivalent), of BD2 scale (A1-A5) <14% or less. Prime with one coat wood primer (UC2) with an overcoating time of 16 hours and finish with two coats Valvagio Satin (VLO) with 16 hours drying time between coats, for a maintenance cycle of 3 years.

GENERAL:

- IRONMONGERY: as per ironmongery schedule
- NOTE:**
Specialist / Manufacturer to take on site measurements prior to manufacture.
No scaling to be done from schedule drawings.

MDA ARCHITECTS
ISSUED FOR CONSTRUCTION
DRAWING NUMBER:

DC-AR-1707

DATE:

04.10.2022

Revision:

00
